

Final Assessment - Alternative Assessment

Semester	202520	Division	CIS
Assessment title in Syllabus	Final_Project_Portfolio	Program	Bachelor of Information Technology/ Bachelor of Information Systems

Course Code	CIS 3603		
Course Title	PROJECT MANAGEMENT		
Course Instructor	Mr. Asem Kasem	CRN	22931
Assessment	Project Deliverable 3: Project Execution, Monitoring and Closing Report	Submission Date	Week 14

Student Declaration:

Academic Integrity Statement

In accordance with the HCT Academic Integrity Policy

- Students are required to refrain from all forms of academic integrity breaches as defined and explained by HCT.
- A student found guilty of having committed acts of academic integrity breach(es) will be subject to the relevant sanctions as outlined by HCT.

إفادة النزاهة الأكاديمية

وفقاً لسياسة كليات التقنية العليا للنزاهة الأكاديمية

- على الطلبة الالتزام بلوائح وقواعد النزاهة الأكاديمية، كما هو مبين وموضح في السياسات والإجراءات الخاصة بكليات التقنية العليا.
- في حالة ارتكاب الطالب أي شكل من أشكال الإخلال بالنزاهة الأكاديمية، سيتعرض إلى العقوبات الموضحة في السياسات ذات الصلة.

This assignment is entirely my/our own work except where I have duly acknowledged other sources in the text and listed those sources at the end of the assignment. I have not previously submitted this work to the HCT, or any other entity. I understand that I may be orally examined on my submission.

Student HCT ID(s):	H00535836	H00535463	H00495503	H00469084	H00
Student Name(s):	Maryam Ali Abdulla	Jawaher Alhosani	Amna Saif	Shamsa Saeed	
Student Signature					

Chatbot (e.g. ChatGPT) statement

This submission allows you to use AI generated tools, but the prompt used must be stated and the response must be in red font. Include References to ChatGPT as per project guidelines

Instructions

Remove instructions and hints from the template before submitting the final report to BBLearn.

Project Execution and Monitoring Report

Introduction to Project Execution and Monitoring and Control

The project execution phase is where the planned tasks are carried out and the system features are developed. The FuturePark Mobile Application project has been divided into three sprints using an Agile (Scrum) methodology. There were design, development, and testing tasks in every sprint.

During execution, the team followed simple Scrum practices such as daily meetings to discuss progress and any issues. Tasks were selected from the sprint backlog and completed gradually.

The project was monitored using MS Project by tracking task progress, durations, and resource usage. This helped the team compare planned work with actual progress and make adjustments when needed.

Change Management

An Agile methodology was used to manage changes in this project. The current sprint did not immediately include any new requirements or modifications. Rather, it was added to the product backlog.

The Product Owner reviewed the changes and decided their priority. Important changes were then included in the next sprint and implemented accordingly.

This strategy allowed for flexibility to enhance the system while keeping the team organised and preventing delays.

Earned Value Analysis

Current Scenario

The FuturePark Mobile Application project is currently at the end of Sprint 2 out of a total of three planned sprints. The project follows the Agile methodology, with each sprint lasting two weeks, making the total planned duration six weeks. The total project budget is AED 80,000.

By the end of Sprint 2, the team originally planned to complete 6 out of 10 user stories, with a planned budget usage of AED 48,000. However, the actual progress shows that only 5 user stories have been completed. In terms of cost, the value of completed work is estimated at AED 40,000, while the team has actually spent AED 45,000 so far.

This indicates that the project is slightly behind schedule and experiencing cost inefficiency. The delay and increased spending are mainly due to additional time required for testing activities during Sprint 2, which slowed down development progress.

With only one sprint remaining, the team still needs to complete 5 user stories, which represents half of the total project scope. This increases the pressure on the final sprint and introduces a higher risk of not meeting the planned timeline and budget.

Project Performance

The following Earned Value Analysis (EVA) metrics are calculated based on the scenario above. All values are in AED.

Key Inputs:

- BAC (Budget at Completion) = AED 80,000
- PV (Planned Value) = AED 48,000
- EV (Earned Value) = AED 40,000
- AC (Actual Cost) = AED 45,000

Earned Value Formulas Reference (as per course lecture)

Term	Formula	Description	Interpretation
PV	$PV = \text{Planned \% Complete} \times BAC$	Value of work planned to be completed by a specific time	-
EV	$EV = \text{Actual \% Complete} \times BAC$	Value of work completed by a specific time	-
CV	$CV = EV - AC$	Difference between earned value and actual cost	CV > 0: Under budget; CV < 0: Over budget
SV	$SV = EV - PV$	Difference between earned value and planned value	SV > 0: Ahead of schedule; SV < 0: Behind schedule
CPI	$CPI = EV / AC$	Measure of cost efficiency	CPI = 1: On budget; CPI < 1: Over budget; CPI > 1: Under budget
SPI	$SPI = EV / PV$	Measure of schedule efficiency	SPI = 1: On schedule; SPI < 1: Behind; SPI > 1: Ahead
EAC	$EAC = BAC / CPI$	Expected total cost of completing all work	Forecast of total cost based on current performance
ETC	$ETC = EAC - AC$	Expected cost to finish all remaining work	Additional cost required to complete the project
VAC	$VAC = BAC - EAC$	Difference between budget at completion and estimate at completion	VAC > 0: Under budget; VAC < 0: Over budget
TCPI	$TCPI = (BAC - EV) / (BAC - AC)$	Cost performance required to meet the management goal	TCPI < 1: Easier to complete; TCPI > 1: More challenging

Source: CIS3603 Project Management Lecture – Project Monitoring (Week 13)

1. Cost Variance (CV):

$$CV = EV - AC = 40,000 - 45,000 = \text{AED } -5,000$$

Interpretation: The project is over budget by AED 5,000. The negative CV indicates that the team has spent more than the value of work completed.

2. Schedule Variance (SV):

$$SV = EV - PV = 40,000 - 48,000 = \text{AED } -8,000$$

Interpretation: The project is behind schedule by AED 8,000 worth of planned work. In Agile terms, this means 1 user story behind the planned velocity.

3. Cost Performance Index (CPI):

$$CPI = EV / AC = 40,000 / 45,000 = 0.89$$

Interpretation: For every AED 1 spent, only AED 0.89 worth of work is being delivered. $CPI < 1$ indicates cost inefficiency.

4. Schedule Performance Index (SPI):

$$SPI = EV / PV = 40,000 / 48,000 = 0.83$$

Interpretation: The team is working at 83% of the planned schedule efficiency. $SPI < 1$ confirms the project is behind schedule.

5. Estimate at Completion (EAC):

$$EAC = BAC / CPI = 80,000 / 0.89 = \text{AED } 89,888$$

Interpretation: If the current cost performance continues, the project is forecasted to cost AED 89,888, which is AED 9,888 over the original budget.

6. Estimate to Complete (ETC):

$$ETC = EAC - AC = 89,888 - 45,000 = \text{AED } 44,888$$

Interpretation: The team needs approximately AED 44,888 more to complete the remaining work in Sprint 3.

7. Variance at Completion (VAC):

$$VAC = BAC - EAC = 80,000 - 89,888 = \text{AED } -9,888$$

Interpretation: The project is expected to exceed the budget by AED 9,888 at completion if no corrective actions are taken.

8. To-Complete Performance Index (TCPI):

$$TCPI = (BAC - EV) / (BAC - AC) = (80,000 - 40,000) / (80,000 - 45,000) = 40,000 / 35,000 = 1.14$$

Interpretation: The team must perform at 1.14 times the current efficiency to complete the remaining work within the original budget. This is a challenging target, reinforcing the need for corrective action.

Agile Burndown Chart Analysis:

In the Agile context, the Burndown Chart is the primary performance tracking tool. The chart below compares the Ideal Burndown Line against the Actual Burndown based on remaining story points per sprint.

Total User Stories: 10 | Story Points per Story: 8 | Total Story Points: 80

- Sprint 0 (Start): Ideal = 80 SP remaining | Actual = 80 SP remaining
- End of Sprint 1: Ideal = 53 SP remaining | Actual = 48 SP remaining (team ahead of schedule)

- End of Sprint 2: Ideal = 27 SP remaining | Actual = 40 SP remaining (team behind schedule)
- End of Sprint 3 (Projected): Ideal = 0 SP | Actual target = 0 SP (requires sprint 3 velocity of 40 SP)

The burndown chart shows that the actual line crossed above the ideal line at Sprint 2, indicating a slowdown due to the additional testing effort. The team must increase velocity in Sprint 3 to complete all remaining 5 user stories (40 story points) on time.

Summary of EVA Metrics:

- PV = AED 48,000 | EV = AED 40,000 | AC = AED 45,000
- CV = -5,000 | SV = -8,000 | CPI = 0.89 | SPI = 0.83
- EAC = AED 89,888 | ETC = AED 44,888 | VAC = -AED 9,888 | TCPI = 1.14

Overall, the FuturePark project is currently behind schedule and over budget. Corrective actions are recommended to improve both cost and schedule performance in Sprint 3.

EVM in Agile Approach – Performance Measurement

The Performance Measurement Baseline (PMB) is determined at the release level in Agile projects. For every release, the BAC is represented by the PMB. The following fundamental metrics are used to monitor success in Agile/Scrum projects, according to the course lecture. At the conclusion of each iteration (sprint), the EVM metrics (EV, PV, and AC) are calculated and correlated with the completion of user stories.

Abbr.	Term	Explanation	Calculation
EPC	Planned (Expected) Percent Complete	Amount of value planned to be delivered in the period	= Current Iteration No. / Total Iterations
PV	Planned Value	Value of work planned at end of the iteration	= EPC x BAC
APC	Actual Percent Complete	Amount of value actually delivered in the period	= Story Points Completed / Total Story Points Planned
EV	Earned Value	Value of work accomplished at end of the iteration	= APC x BAC

Applying Agile EVM to FuturePark – Sprint 2 Analysis

Using the Agile EVM formulas from the course lecture, the FuturePark project sprint metrics are computed as follows:

- BAC = AED 80,000 (total release budget for 10 user stories at AED 8,000 each)
- Total Iterations = 3 | Current Iteration = 2
- EPC (Planned % Complete) = $2/3 = 66.7\%$ → PV = $66.7\% \times 80,000 = \text{AED } 53,360$ (adjusted from scenario PV of AED 48,000 which uses user story ratio of 6/10)
- APC (Actual % Complete) = $5/10 = 50\%$ → EV = $50\% \times 80,000 = \text{AED } 40,000$
- AC = AED 45,000 (actual cost incurred at end of Sprint 2)

These Agile EVM metrics align with the interpretations from the course lecture: $SV < 0$ confirms the release is behind schedule; $CPI < 1$ confirms the release is above the budget; and $TCPI > 1.0$ means it is challenging but possible to complete within the original budget with improved sprint velocity in Sprint 3.

Project Reports

Status Reports

A project status report must cover four essential components, according to the Project Monitoring course lecture (CIS3603 – Week 13): (1) who receives the report; (2) current project data, including money spent and time completed; (3) project progress in terms of time and money using EVM indicators; and (4) project forecasts based on current performance. The FuturePark Mobile Application project's status report is organized as follows.

PROJECT STATUS REPORT

Project Name: FuturePark Mobile Application

Report Date: End of Sprint 2 (Week 4 of 6)

Prepared By: Project Manager

Submitted To: Project Sponsor / Product Owner

Overall Status: AT RISK — Behind Schedule and Over Budget

1. Executive Summary

The FuturePark Mobile Application project's second sprint is coming to a conclusion. Five of the ten planned user stories (or 50% of the project's scope) have been accomplished, and AED 45,000 of the AED 80,000 total budget (or 56% of the budget) has been spent. Regrettably, the project is currently over budget and over schedule, according to our Earned Value Analysis. Before Sprint 3 starts, immediate remedial action is needed to get the project back on schedule.

2. Performance Summary (Earned Value Analysis)

The following key metrics have been computed to assess project performance as of the end of Sprint 2:

- Planned Value (PV) = AED 48,000 — This is what we planned to accomplish by end of Sprint 2.
- Earned Value (EV) = AED 40,000 — This is the actual value of work delivered. We completed 5 user stories instead of the planned 6, leaving us AED 8,000 short of the schedule target.
- Actual Cost (AC) = AED 45,000 — We spent AED 5,000 more than the value of work delivered, indicating cost overrun.

Schedule Performance: The Schedule Variance (SV) is -AED 8,000 and the Schedule Performance Index (SPI) is 0.83. An SPI below 1.0 means we are completing work at only 83% of the planned rate. In Agile terms, we are 1 user story (8 story points) behind our expected velocity. The Burndown Chart confirms this, with the actual line crossing above the ideal line at the end of Sprint 2.

Cost Performance: The Cost Variance (CV) is –AED 5,000 and the Cost Performance Index (CPI) is 0.89. This means that for every AED 1.00 we spend, we are only delivering AED 0.89 worth of work. If this trend continues, the Estimate at Completion (EAC) will reach AED 89,888 exceeding our original budget by AED 9,888 (Variance at Completion = –AED 9,888).

Efficiency Required to Recover: The To-Complete Performance Index (TCPI) is 1.14. This means the team must perform at 114% efficiency for the remainder of the project to deliver within the original AED 80,000 budget. This is an ambitious but achievable target with focused effort and process improvements

3. Root Cause of Variance

The additional testing work needed in Sprint 2 for the Park Navigation and Booking modules is the main reason for the schedule and cost difference. The integration needs for these two improvements were more complicated than anticipated. The number of user stories provided decreased from six to five as a result of the team devoting more time than anticipated on debugging and user acceptance testing. Additionally, the actual cost exceeded the budgeted amount.

4. Corrective Actions Recommended

The following corrective actions are recommended to recover schedule and control costs in Sprint 3:

- 1. Increase Sprint Velocity:** The team must complete all 5 remaining user stories (40 story points) in Sprint 3. To achieve this, testing activities will begin in parallel with development rather than waiting until the end of the sprint, reducing bottlenecks.
- 2. Scope Review with Product Owner:** We recommend a meeting with the product owner to reprioritize the remaining backlog. Lower-priority user stories may be descoped or deferred to a future release if needed to protect the delivery of core features within the budget.
- 3. Daily Stand-up Focus on Blockers:** Sprint 3 daily stand-ups will include a dedicated “blocker review” segment. Any impediment must be escalated within 24 hours to prevent delays from accumulating, as happened in Sprint 2.
- 4. Resource Optimization:** Team members who completed their Sprint 2 tasks early will be reassigned to assist with the remaining high-complexity stories in Sprint 3 to distribute the workload more evenly and improve cost efficiency toward the TCPI target of 1.14.

5. Upcoming Milestones


- Sprint 3 Start: Week 5 — Kickoff planning meeting and backlog refinement session.
- Sprint 3 Review & Demo: Week 6 — Delivery of all remaining 5 user stories and final product demonstration to the Product Owner.
- Project Closure: End of Week 6 — Final documentation, lessons learned, and handover to stakeholders.

6. Conclusion

Even though the FuturePark Mobile Application project is currently over budget (CPI = 0.89) and behind time (SPI = 0.83), things are still manageable. The group has determined specific corrective measures for Sprint 3 and has a thorough grasp of the underlying issues. The project can still produce a high-quality outcome with concentrated work and the suggested process enhancements. A successful project closing will depend on your ongoing support and approval of the suggested corrective actions.

Other Reports

Figure 1 tasks completed:

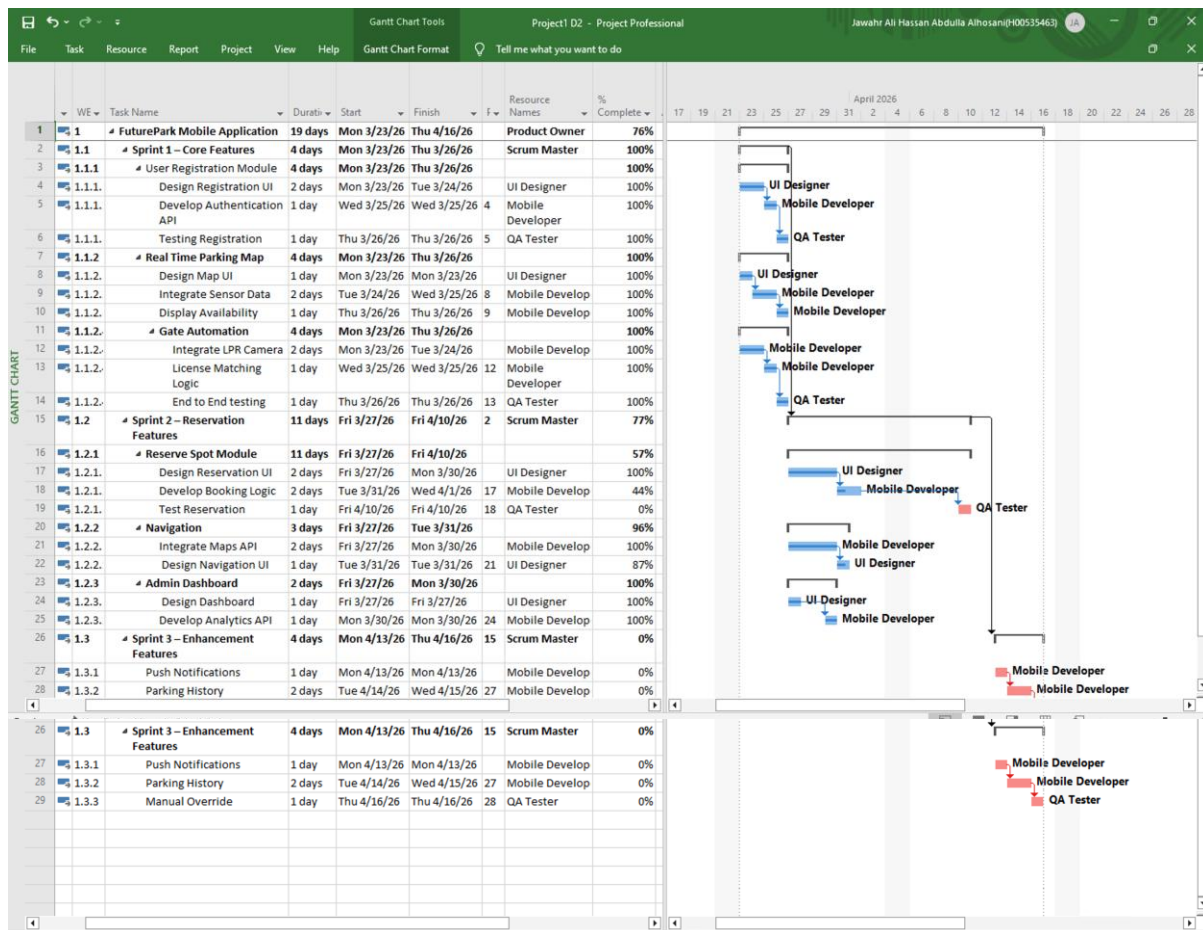

Its showing the WBS and the percentage of completion of each task.

Figure 2 resource usage:

Resource Name	Work	Add New	Details	M	T	W	T	F	S	Mar 29, '26	S	M	T	W	T	F	S	Apr 5, '26	M
Product Owner	152 hrs		Work	8h	8h	8h	8h	8h	3/27/26			8h	8h	8h	8h	8h			8h
FuturePark Mobile Application	152 hrs		Work	8h	8h	8h	8h	8h				8h	8h	8h	8h	8h			8h
Scrum Master	144 hrs		Work	8h	8h	8h	8h	0h				8h	8h	8h	8h	8h			8h
Sprint 1 – Core Features	32 hrs		Work	8h	8h	8h	8h												
Sprint 2 – Reservation Features	80 hrs		Work					0h				8h	8h	8h	8h	8h			8h
Sprint 3 – Enhancement Features	32 hrs		Work																
Mobile Developer	112 hrs		Work	8h	16h	24h	8h	8h				16h	8h						
Develop Authentication API	8 hrs		Work			8h													
Integrate Sensor Data	16 hrs		Work		8h	8h													
Display Availability	8 hrs		Work				8h												
Integrate LPR Camera	16 hrs		Work	8h	8h														
License Matching Logic	8 hrs		Work			8h													
Develop Booking Logic	8 hrs		Work										8h						
Integrate Maps API	16 hrs		Work					8h				8h							
Develop Analytics API	8 hrs		Work									8h							
Push Notifications	8 hrs		Work																
Parking History	16 hrs		Work																
UI Designer	56 hrs		Work	16h	8h			16h				8h	8h						
Design Registration UI	16 hrs		Work	8h	8h														
Design Map UI	8 hrs		Work	8h															
Design Reservation UI	16 hrs		Work					8h				8h							
Design Navigation UI	8 hrs		Work										8h						
Design Dashboard	8 hrs		Work					8h											
QA Tester	32 hrs		Work				16h												
Testing Registration	8 hrs		Work				8h												
End to End testing	8 hrs		Work				8h												

It shows the distribution of the hourly work on each member and relieves the presser on the work.

Figur3 burndown charts:



The burndown chart compares between the plan and the actual work

Introduction to Project Closing

The project closing final step in the project lifecycle, where all project needs are completed and ready to be delivered to the product owner.

In our project we have used both waterfall and agile, which is the hybrid approach. However, we have worked on the adaptive approach (Agile), especially in developing mobile applications and AI algorithms, as this allowed us to continuously take user feedback. The project was split into 3 parts(3sprints) to manage the work more effectively.

For Sprint1, it focused on the core features, including user registration, real-time parking map, and automatic gate access. The goal of this phase was to build a strong foundation and ensure that everything is working perfectly. For Sprint2, it focused on reservation features, which included the parking reservation module, navigation, and admin dashboard. The goal of this sprint was to improve the system's functionality. However, this stage required more time and effort for testing and integration, which caused some delays. And finally, Sprint3 focused on completing the remaining tasks, improving system performance, and preparing the system for final delivery.

For future improvements, we suggest enhancing the system features and improving integration with other HCT systems to increase efficiency. While working on the FuturePark project, we learned the importance of early planning, and the effect of the team communication. The team had successfully completed the main features of the FuturePark to achieve most of the project objectives. Some challenges were faced such as minor delays and technical limitations, but they were managed throughout the project. At the end the system features were integrated and tested together to ensure that the system works as expected. The team confirmed that the main requirements were achieved according to the defined standards, and the project was closed after ensuring stakeholder satisfaction.

The method our group adopted for closing the project:

- Final Sprint Review: delivering the a final demonstration of the complete, integrated the project to all key stakeholders, including the Project Sponsor and the Campus Director, to gain their formal acceptance.

- Final Project Retrospective: Holding a retrospective meeting with the entire project team where we have discussed the project journey, documenting what went well, what did not, and the key lessons learned for future projects.

- Finalizing Documentation: Ensuring all project of the documentation, including the final Product Backlog, technical documents, and user guides, is updated and stored in a central repository for future reference.

- Releasing the Team: Officially closing the project and releasing team members to their next assignments, after celebrating the success and effort of the team.

This structured approach ensures a smooth transition from development to operations.

Achievement of Objectives

The FuturePark project has achieved most of the objectives in the Project Charter. Because the system provides the necessary tools to achieve the goals in the Project Charter. It had successfully reduced the time required to search for an empty parking spot. This objective was achieved by implementing the real-time parking system, where sensors send notifications to the system whenever a parking spot is available. This allows users, including students and faculty, to directly view where the available parking spots and the system also guide users to the parking location, saving users time and reducing the traffic in the campus parking area.

Regarding peak morning hours, the objective of reducing congestion by 40% was partially achieved. The system helps organize parking usage and reduce unnecessary movement on campus.

In principle, we have reached the goals of reducing the traffic in the morning period by 40% and the search for positions will be less than 5 minutes , and also after this program is used for a whole semester, it will be determined and confirmed whether we have 100% reached our goals or not. Overall, the FuturePark project successfully achieved its main objectives in the Project Charter.

Lessons Learned

Lesson 1: The Importance of Detailed Task Estimation

Challenge: In Sprint 1, we planned our tasks but our time estimates were too optimistic. For example, we estimated the "Integrate LPR Camera" task would take one day, but it actually took two days because of unexpected technical issues. This small delay created pressure at the end of the sprint.

Action Taken: Before starting Sprint 2, we held a special 30-minute meeting. We discussed why our first estimates were wrong. We decided to break down big tasks into smaller, more manageable sub-tasks. For the "Develop Booking Logic" task in Sprint 2, we broke it down into "Design Database," "Write API," and "Test Logic," and estimated each part separately.

Impact: This action made our planning for Sprint 2 and Sprint 3 much more accurate. We had a clearer idea of the effort required, which reduced stress and helped us manage our time better.

Recommendation for Future Projects: We recommend always breaking down features into the smallest possible technical tasks before estimating the time. We also suggest adding a small buffer (around 15-20%) to the schedule for unexpected problems.

Lesson 2: The Power of Daily Communication

Challenge: At the beginning of the project, team members worked on their tasks separately. One team member was struggling with a coding problem but did not ask for help for a full day, hoping to solve it alone. This caused a delay and wasted valuable time.

Action Taken: We realized we needed better communication. We made our Daily Scrum meeting a strict rule. Every morning at 9 AM, each member had to answer three questions: What did you do yesterday? What will you do today? Are you facing any problems?

Impact: The Daily Scrum meeting was a game-changer. The team member who was stuck immediately got help from another developer. Problems were identified and solved within hours instead of days. This improved our teamwork and made us work faster.

Recommendation for Future Projects: We strongly recommend holding a short, daily stand-up meeting. It is the most effective way to keep the team synchronized, solve problems quickly, and ensure everyone feels supported.

Lesson 3: The Value of Stakeholder Feedback in Sprints

Challenge: During the development of the "Real-time Parking Map," our team designed an interface that we thought was very good. However, when we showed it to a few student users informally, they found it confusing to read. If we had continued without this feedback, we would have built a feature that users did not like.


Action Taken: We immediately took their feedback and simplified the map's design, using clearer colors and bigger icons. More importantly, we made it a rule to invite our Project Sponsor and a small group of end-users to every Sprint Review meeting. This gave them a formal opportunity to see the actual working software and give their opinions.

Impact: This action ensured that the final product was not just technically correct, but also user-friendly and valuable to the people who will actually use it. It saved us from having to make big, expensive changes at the end of the project.

Recommendation for Future Projects: Never assume you know what the user wants. We recommend involving stakeholders and end-users regularly by demonstrating working software at the end of every sprint. Their feedback is essential for building a successful product.

Planning, Communication and collaboration

Evidence 1: sharepoint link




https://hctuae-my.sharepoint.com/:w/g/personal/h00535836_hct_ac_ae/IQDj87xTXPt9QphCSXBX6BwTAXa5S YO3NzERm2yGxaZ5C4I?e=pOoV0A

Evidence 2: Work Distribution Table


Team Member	Student ID	Assigned Sections for Deliverable 3	Role/Focus
Shamsa Saeed Altemelji	H00469084	- Introduction to Project Execution - Change Management - Current Scenario	Phase 1: Execution Setup
Amna Saif Al Ali	H00495503	- Project Performance (EVA) - Status Reports - Other Reports (MS Project) - Introduction to Project Closing - Achievement of Objectives - Use of Project Management	Phase 2: Monitoring & Analysis
Jawahar Ali Althosani	H00535463	- Software - Lessons Learned - Planning, Communication & Collaboration - Self and Peer Evaluation	Phase 3: Reporting & Closing
Maryam Ali Alali	H00535836	Overall Project Management	Phase 4: Reflection & Finalization

Evidence 3: Ms Teams Chat Capture

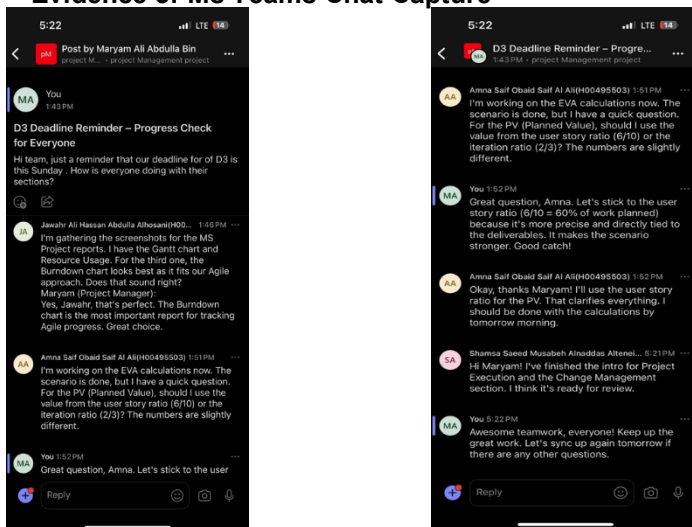

Use of Project Management Software

Network diagram:

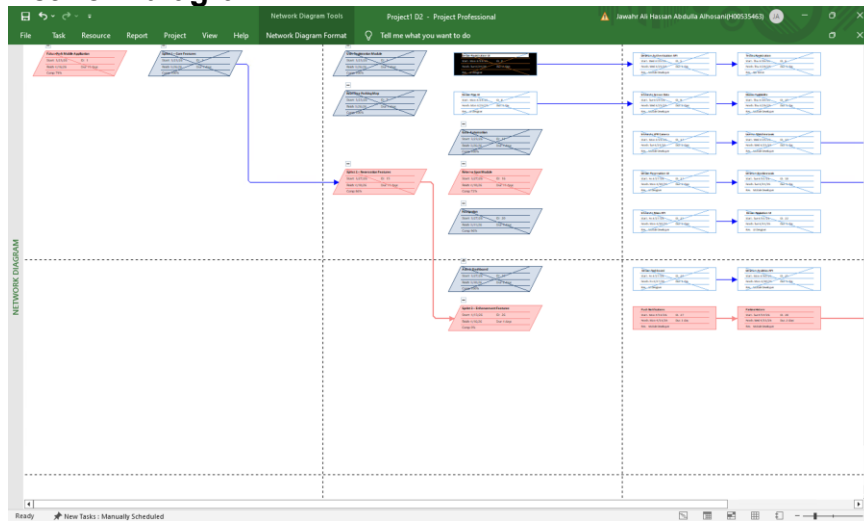


The Network diagram helps us to identify the sequence of project tasks and their dependencies. It allows the team to understand task relationships and calculate the critical path. We used it in D2 to find the critical path for sprint one. The network diagram shows all sub-task start and end dates, helping us understand their durations. If there is any delay, the entire sprint will also be delayed. This lets us identify risks early and take action to reduce the impact of delays.

Task list & Auto-scheduling:

	Task Mode	WBS	Task Name	Duration	Start	Finish	Resource Names	% Complete
1		1	FuturePark Mobile Application	19 days	Mon 3/23/26	Thu 4/16/26	Product Owner	79%
2		1.1	Sprint 1 – Core Features	4 days	Mon 3/23/26	Thu 3/26/26	Scrum Master	100%
3		1.1.1	User Registration Module	4 days	Mon 3/23/26	Thu 3/26/26		100%
4		1.1.1.1	Design Registration UI	2 days	Mon 3/23/26	Tue 3/24/26	UI Designer	100%
5		1.1.1.2	Develop Authentication API	1 day	Wed 3/25/26	Wed 3/25/26	Mobile Develop	100%
6		1.1.1.3	Testing Registration	1 day	Thu 3/26/26	Thu 3/26/26	QA Tester	100%
7		1.1.2	Real Time Parking Map	4 days	Mon 3/23/26	Thu 3/26/26		100%
8		1.1.2.1	Design Map UI	1 day	Mon 3/23/26	Mon 3/23/26	UI Designer	100%
9		1.1.2.2	Integrate Sensor Data	2 days	Tue 3/24/26	Wed 3/25/26	Mobile Develop	100%
10		1.1.2.3	Display Availability	1 day	Thu 3/26/26	Thu 3/26/26	Mobile Develop	100%
11		1.1.2.4	Gate Automation	4 days	Mon 3/23/26	Thu 3/26/26		100%
12		1.1.2.4.1	Integrate LPR Camera	2 days	Mon 3/23/26	Tue 3/24/26	Mobile Develop	100%
13		1.1.2.4.2	License Matching Logic	1 day	Wed 3/25/26	Wed 3/25/26	Mobile Develop	100%
14		1.1.2.4.3	End to End testing	1 day	Thu 3/26/26	Thu 3/26/26	QA Tester	100%
15		1.2	Sprint 2 – Reservation Features	11 days	Fri 3/27/26	Fri 4/10/26	Scrum Master	96%
16		1.2.1	Reserve Spot Module	11 days	Fri 3/27/26	Fri 4/10/26		72%
17		1.2.1.1	Design Reservation UI	2 days	Fri 3/27/26	Mon 3/30/26	UI Designer	100%
18		1.2.1.2	Develop Booking Logic	1 day	Tue 3/31/26	Tue 3/31/26	Mobile Develop	87%
19		1.2.1.3	Test Reservation	1 day	Fri 4/10/26	Fri 4/10/26	QA Tester	0%
20		1.2.2	Navigation	3 days	Fri 3/27/26	Tue 3/31/26		96%
21		1.2.2.1	Integrate Maps API	2 days	Fri 3/27/26	Mon 3/30/26	Mobile Develop	100%
22		1.2.2.2	Design Navigation UI	1 day	Tue 3/31/26	Tue 3/31/26	UI Designer	87%
23		1.2.3	Admin Dashboard	2 days	Fri 3/27/26	Mon 3/30/26		100%
24		1.2.3.1	Design Dashboard	1 day	Fri 3/27/26	Fri 3/27/26	UI Designer	100%
25		1.2.3.2	Develop Analytics API	1 day	Mon 3/30/26	Mon 3/30/26	Mobile Develop	100%
26		1.3	Sprint 3 – Enhancement Features	4 days	Mon 4/13/26	Thu 4/16/26	Scrum Master	0%
27		1.3.1	Push Notifications	1 day	Mon 4/13/26	Mon 4/13/26	Mobile Develop	0%
28		1.3.2	Parking History	2 days	Tue 4/14/26	Wed 4/15/26	Mobile Develop	0%
29		1.3.3	Manual Override	1 day	Thu 4/16/26	Thu 4/16/26	QA Tester	0%

The Task list and the Auto-scheduling feature helped us to automatically calculate the start and finish dates when we entered the duration. It also gave us a clear WBS numbering structure in splitting the Sprint tasks. Finally, we could assign a resource name and track the percentage of complete task, which helped in managing and organizing the project effectively.

Gantt chart:

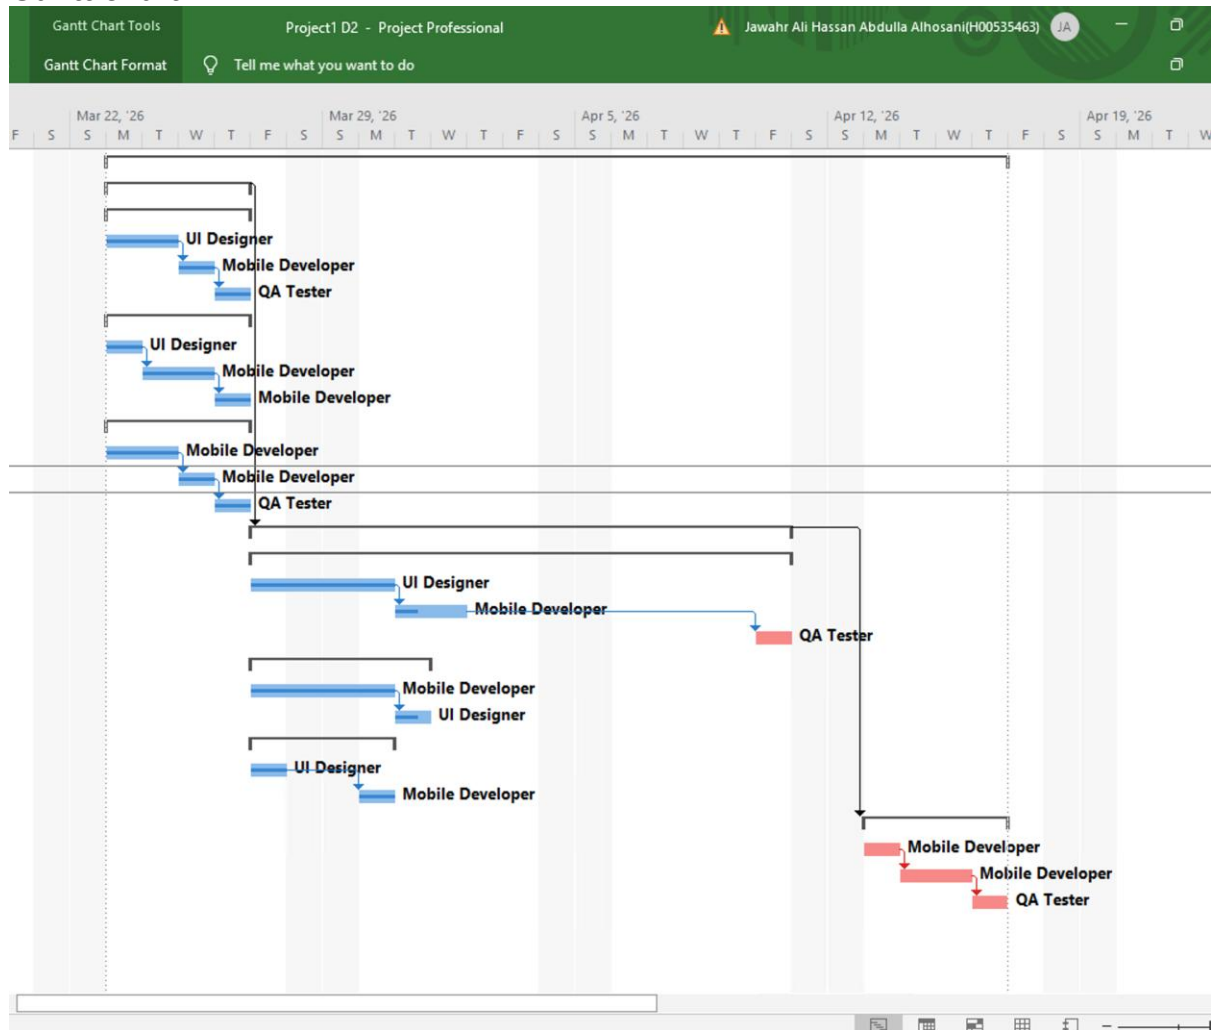

We have used the Gantt chart to visually show the project schedule and project tracking. Where it shows what should be done, how long each task will take, the start and end date for each task, dependency, where it shows which tasks should be done first before the other (Predecessors), and the completeness of each task. This helped the team monitor deadlines and identify potential delays.

Self and Peer Evaluation

To ensure a fair and constructive evaluation, our team agreed to assess each other based on three simple criteria.

Evaluation Criteria:

1. **Responsibility & Timeliness:** Did the team member complete their assigned tasks on time and to a high standard?
2. **Communication & Collaboration:** Did the team member communicate clearly, ask for help when needed, and actively participate in team discussions?
3. **Quality of Work:** Was the work submitted well-researched, accurate, and aligned with the project requirements?

1. Self-Evaluation (Maryam Ali Alali)

My Performance: I believe I performed my role as Project Manager effectively. I focused on organizing the work for each deliverable, setting clear deadlines, and making sure everyone understood their tasks. I tried to be available to answer questions, as shown in our team chat when Amna had a question about the EVA calculations. One area I could improve is in documenting meeting notes more formally after our calls. Overall, I feel I contributed positively to the project's success.

2. Peer Evaluation (Evaluation of Team Members)

As the Project Manager, I had the opportunity to work closely with every team member. Here is my evaluation of my peers:

Shamsa Saeed Alteneiji (H00469084):

Evaluation: Shamsa was excellent. She took responsibility for her sections (Project Execution and Change Management) and delivered them ahead of schedule. Her work was clear, accurate, and perfectly matched the Agile methodology we chose. She was a reliable and proactive team member.

Amna Saif Al Ali (H00495503):

Evaluation: Amna did an outstanding job on one of the most difficult parts of the project: the Earned Value Analysis. Her work was incredibly detailed and accurate. What impressed me most was her communication. When she was unsure about a calculation, she asked for clarification immediately, which prevented errors and showed great collaboration.

Jawahr Ali Alhosani (H00535463):

Evaluation: Jawahr's contribution was fantastic. She handled multiple sections related to project closing and software reports. She took the initiative to find the correct MS Project reports (like the Burndown Chart) that best fit our project. Her work was well organized and showed a great understanding of how to connect the practical software side with the theoretical report requirements.

Overall Team Performance: I am very proud of our team. Everyone took their roles seriously, supported each other, and was committed to producing high quality work. Our strong communication and collaboration were the main reasons for our success in this project.

End of Documentation
